

DEUTSCHE BANK INDIA

Retail Banking — Digital Payments

PRODUCT BACKLOG

Sprint-Sequenced Release Plan

UPI Enablement Platform

52 User Stories Sequenced Across 8 Sprints and 2 Releases

Document Version: 1.0 (Draft)

Classification: Internal / Confidential

Prepared by: Aniket Saraf

Date: July 2026

Table of Contents

(Right-click and select "Update Field" in Microsoft Word to populate.)

Table of Contents 2

1. Planning Assumptions..... 3

2. Release Plan 4

3. Sprint 0 — Environment & Enablement 5

4. Sprint-by-Sprint Plan..... 6

Sprint 1 — Registration (Epic-01) 6

Sprint 2 — Account Linking & PIN Setup (Epic-02, part of Epic-03)..... 6

Sprint 3 — PIN Lifecycle & Notification Infrastructure (rest of Epic-03, start of Epic-09) 7

Sprint 4 — Send Money — Core Payment Methods (start of Epic-04) 7

Sprint 5 — Send Money — Risk Controls & Resilience (rest of Epic-04, rest of Epic-07)..... 7

Sprint 6 — Collect Requests & Transaction History (Epic-05, start of Epic-08)..... 8

Sprint 7 — QR Payments & History/Notification Completion (Epic-06, rest of Epic-08/09) 8

Sprint 8 — Dispute Management & Remaining Backlog (Epic-10, backlog polish) 8

5. Backlog Management Notes..... 10

5.1 Velocity Risk 10

5.2 Backlog Grooming Cadence 10

5.3 Deferred / Out-of-Backlog Items..... 10

1. Planning Assumptions

- Sprint length: 2 weeks.
- Assumed team velocity: ~20 story points per sprint (Fibonacci scale as defined in the Product Backlog — User Stories deliverable).
- Sequencing respects functional dependency: Registration → Account Linking → PIN → Send Money → Collect/QR → History/Notifications → Dispute, since later modules reuse earlier ones (e.g., Collect Requests reuse the Send Money authorisation logic).
- NPCI/PSP certification, CBS API readiness, and infrastructure/DevOps setup run as a parallel workstream alongside sprint delivery, not represented as backlog stories — see the Risk Register (R-REG-01, R-TEC-01, R-TEC-02, R-PRJ-01) for the risks this creates to the dates below.
- A 'Sprint 0' precedes Sprint 1 for environment setup, CI/CD, PSP sandbox access, and API contract baselining; it carries no story points and is not counted in velocity.
- Sprint numbers below are relative, not calendar dates, since the actual start date depends on PSP partner onboarding completion (BRD Section 5.5 dependencies).

2. Release Plan

The backlog is delivered across two releases. Release 1 constitutes a viable MVP covering all Must Have functional scope; Release 2 completes the remaining Should/Could Have scope and the two modules (QR Payments, Dispute Management) that, while important, are not required for an initial limited launch.

Release	Sprints	Scope	Go-Live Readiness Gate
Release 1 — MVP	Sprint 0 to Sprint 6	Registration, Account Linking, PIN Management, Send Money (all methods), Balance Check, Collect Requests, Transaction History, core Notifications	NPCI production certification; UAT exit criteria (BRD 17.4) met for all Release 1 modules
Release 2 — Full Scope	Sprint 7 to Sprint 8	QR Payments, Dispute Management, remaining notification preferences, PDF export, QR share/download	Release 1 stable in production for a minimum stabilisation period (recommended 2–4 weeks) before Release 2 go-live

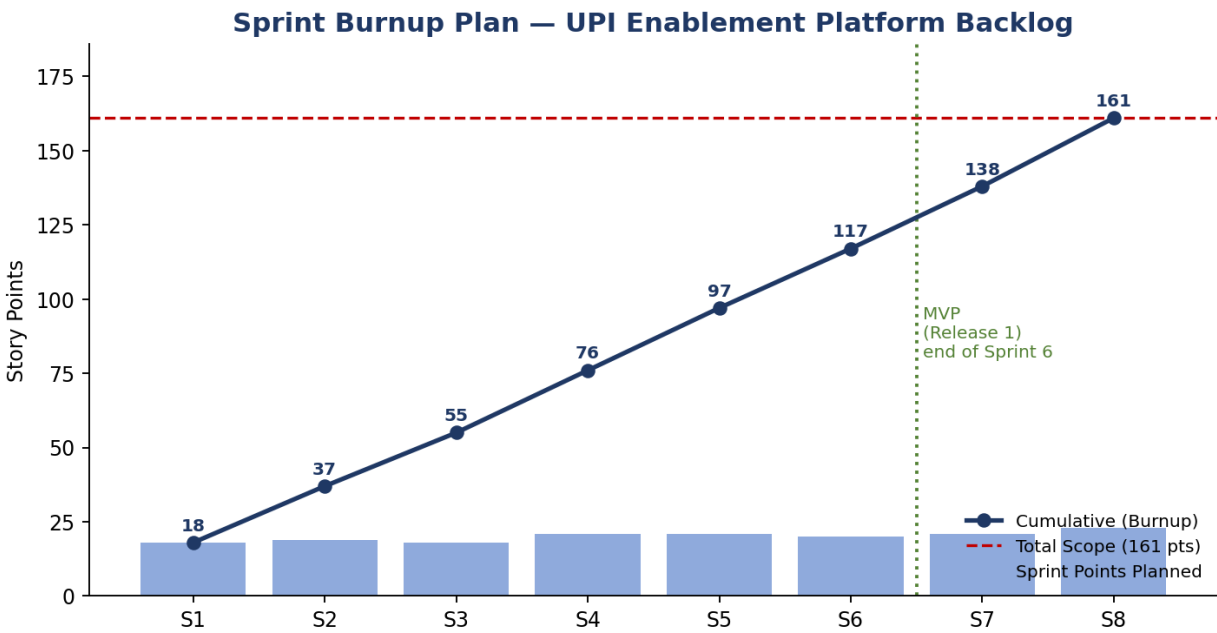


Figure 1 — Planned sprint burnup against the full 161-point backlog, with the Release 1 (MVP) boundary marked at the end of Sprint 6.

3. Sprint 0 — Environment & Enablement

Sprint Goal: Establish the technical and vendor foundation required before feature development begins.

Workstream	Activity
DevOps	CI/CD pipeline setup for mobile app, API gateway, and PSP switch adapter layer
Integration	PSP partner sandbox access provisioned; initial connectivity test to NPCI UAT environment
Database	Baseline schema migration from the ERD (Core Profile & Account entities first)
API Design	API Integration Specification reviewed and baselined with Integration Team and API Developers
Security	Encryption key/certificate provisioning for on-device PIN encryption and mTLS between internal services

4. Sprint-by-Sprint Plan

Sprint 1 — Registration (Epic-01)

Sprint Goal: A customer can complete UPI registration end-to-end in the NPCI sandbox environment.

Story ID	Story (Brief)	Pts
US-01	Register for UPI from within the mobile app	3
US-02	Mobile number verified via OTP	3
US-03	Explicit consent captured before data sharing	2
US-04	Select eligible accounts and default during registration	5
US-05	Success confirmation with assigned VPA	2
US-06	Customise UPI ID handle	3

Sprint Total: 18 points

Notes: Depends on CIF/CBS account discovery API being available per Sprint 0 baseline; if delayed, US-04 may slip to Sprint 2.

Sprint 2 — Account Linking & PIN Setup (Epic-02, part of Epic-03)

Sprint Goal: A registered customer can manage linked accounts and complete initial PIN setup.

Story ID	Story (Brief)	Pts
US-07	View eligible accounts for linking	2
US-08	Link an additional eligible account	3
US-09	Remove a linked account	2
US-10	Blocked from removing default without reassignment	2
US-11	Change default account	2
US-12	Set UPI PIN via debit card validation	5
US-13	Set UPI PIN via Aadhaar-OTP alternate path	3

Sprint Total: 19 points

Sprint 3 — PIN Lifecycle & Notification Infrastructure (rest of Epic-03, start of Epic-09)

Sprint Goal: PIN reset/change/lockout fully operational; core notification dispatch is live ahead of payment features.

Story ID	Story (Brief)	Pts
US-14	Reset a forgotten PIN without old PIN	3
US-15	Change existing PIN with old-PIN validation	2
US-16	Profile locks after 3 incorrect PIN attempts	5
US-17	Clear unlock path after lockout	2
US-42	Real-time payment success/failure notifications	3
US-44	Non-optional security alert notifications	3

Sprint Total: 18 points

Notes: Notification dispatch infrastructure (US-42, US-44) is pulled forward because every subsequent payment story depends on it for its own acceptance criteria.

Sprint 4 — Send Money — Core Payment Methods (start of Epic-04)

Sprint Goal: A registered customer can send money via all four core methods and check account balance.

Story ID	Story (Brief)	Pts
US-18	Send money via recipient mobile number	5
US-19	Send money via UPI ID	5
US-20	Send money via bank account number and IFSC	5
US-21	Self-transfer between own linked accounts	3
US-35	Check account balance from the UPI module	3

Sprint Total: 21 points

Notes: Highest-risk sprint from a technical standpoint — first real dependency on CBS debit/credit posting and PSP switch NPCI routing (see R-TEC-01, R-TEC-02 in the Risk Register).

Sprint 5 — Send Money — Risk Controls & Resilience (rest of Epic-04, rest of Epic-07)

Sprint Goal: Transaction limits, fraud screening, and timeout reconciliation are enforced; balance check is hardened.

Story ID	Story (Brief)	Pts
US-22	Blocked when amount exceeds transaction/daily limit	3
US-23	Risky transactions screened in real time by fraud engine	5
US-24	Timed-out transactions automatically reconciled/reversed	8
US-36	Balance enquiries always require fresh PIN authentication	2
US-37	Daily balance-check cap enforcement	1

Sprint Total: 19 points

Notes: US-24 (8 points) is the single largest story in the backlog — the deferred reconciliation logic touches PSP Switch, NPCI, CBS, and Notification Service together.

Sprint 6 — Collect Requests & Transaction History (Epic-05, start of Epic-08)

Sprint Goal: Customers can create/approve/reject collect requests and view/filter their transaction history. Marks the end of Release 1 (MVP) scope.

Story ID	Story (Brief)	Pts
US-25	Request money from another UPI user	3
US-26	Approve a collect request with PIN	5
US-27	Reject a collect request	2
US-28	Unpaid requests expire automatically after 24 hours	2
US-29	Send limited reminders for a pending request	2
US-38	View recent UPI transactions (default 6-month view)	3
US-39	Filter transaction history by multiple criteria	3

Sprint Total: 20 points

Notes: End of Release 1 (MVP). Cumulative scope at this point: 117 of 161 points (~73%).

Sprint 7 — QR Payments & History/Notification Completion (Epic-06, rest of Epic-08/09)

Sprint Goal: Static/dynamic QR generation and scan-to-pay are live; remaining history and notification preference stories are completed.

Story ID	Story (Brief)	Pts
US-30	Generate a static QR code	3
US-31	Generate a dynamic QR with a fixed amount	3
US-32	Scan a QR code to pay	5
US-33	Merchant QR codes validated before payment	3
US-40	View full transaction detail with NPCI reference	2
US-45	Opt out of marketing notifications only	2
US-46	Notification centre to review past alerts	3

Sprint Total: 21 points

Notes: First Release 2 sprint. QR reuses the Send Money authorisation path built in Sprints 4–5, reducing integration risk relative to Sprint 4.

Sprint 8 — Dispute Management & Remaining Backlog (Epic-10, backlog polish)

Sprint Goal: Full dispute lifecycle is live; remaining Could Have polish items are delivered to close out the backlog.

Story ID	Story (Brief)	Pts
US-47	Raise a dispute against a transaction	5
US-48	Attach supporting evidence to a dispute	2
US-49	Track dispute status and NPCI reference number	2
US-50	Operations reviews and updates dispute investigations	3

Story ID	Story (Brief)	Pts
US-51	View refund status when a dispute is upheld	3
US-52	Overdue disputes automatically escalated	3
US-34	Save or share a generated QR code	2
US-41	Export transaction history as a PDF	3

Sprint Total: 23 points

Notes: End of Release 2 (Full Scope). Cumulative scope: 161 of 161 points (100%).

5. Backlog Management Notes

5.1 Velocity Risk

The 20-point/sprint velocity assumption is unvalidated against this specific team's actual throughput until Sprint 1–2 are complete. Re-baseline the remaining sprint plan after Sprint 2 using actual velocity; a variance of $\pm 20\%$ would shift the Release 1 MVP boundary by roughly one sprint in either direction.

5.2 Backlog Grooming Cadence

- Sprint planning at the start of each sprint, re-confirming story readiness (acceptance criteria, dependencies) before commitment.
- Mid-sprint backlog refinement session for the next 1–2 sprints' stories, particularly to validate NPCI/PSP dependencies are on track.
- Sprint review/retrospective at the end of each sprint, feeding any newly identified stories or re-prioritisation back into this backlog.

5.3 Deferred / Out-of-Backlog Items

FR-TXN-12 (save favourite payee) and FR-TXN-13 (payment note/remark) remain Could Have items not currently scheduled in Sprints 1–8, per the Requirement Traceability Matrix gap analysis. These may be pulled into a future sprint opportunistically if team capacity allows, or formally deferred to a post-launch enhancement backlog.
